





SECTION 1 - DUBNÁ SKALA - TURANY



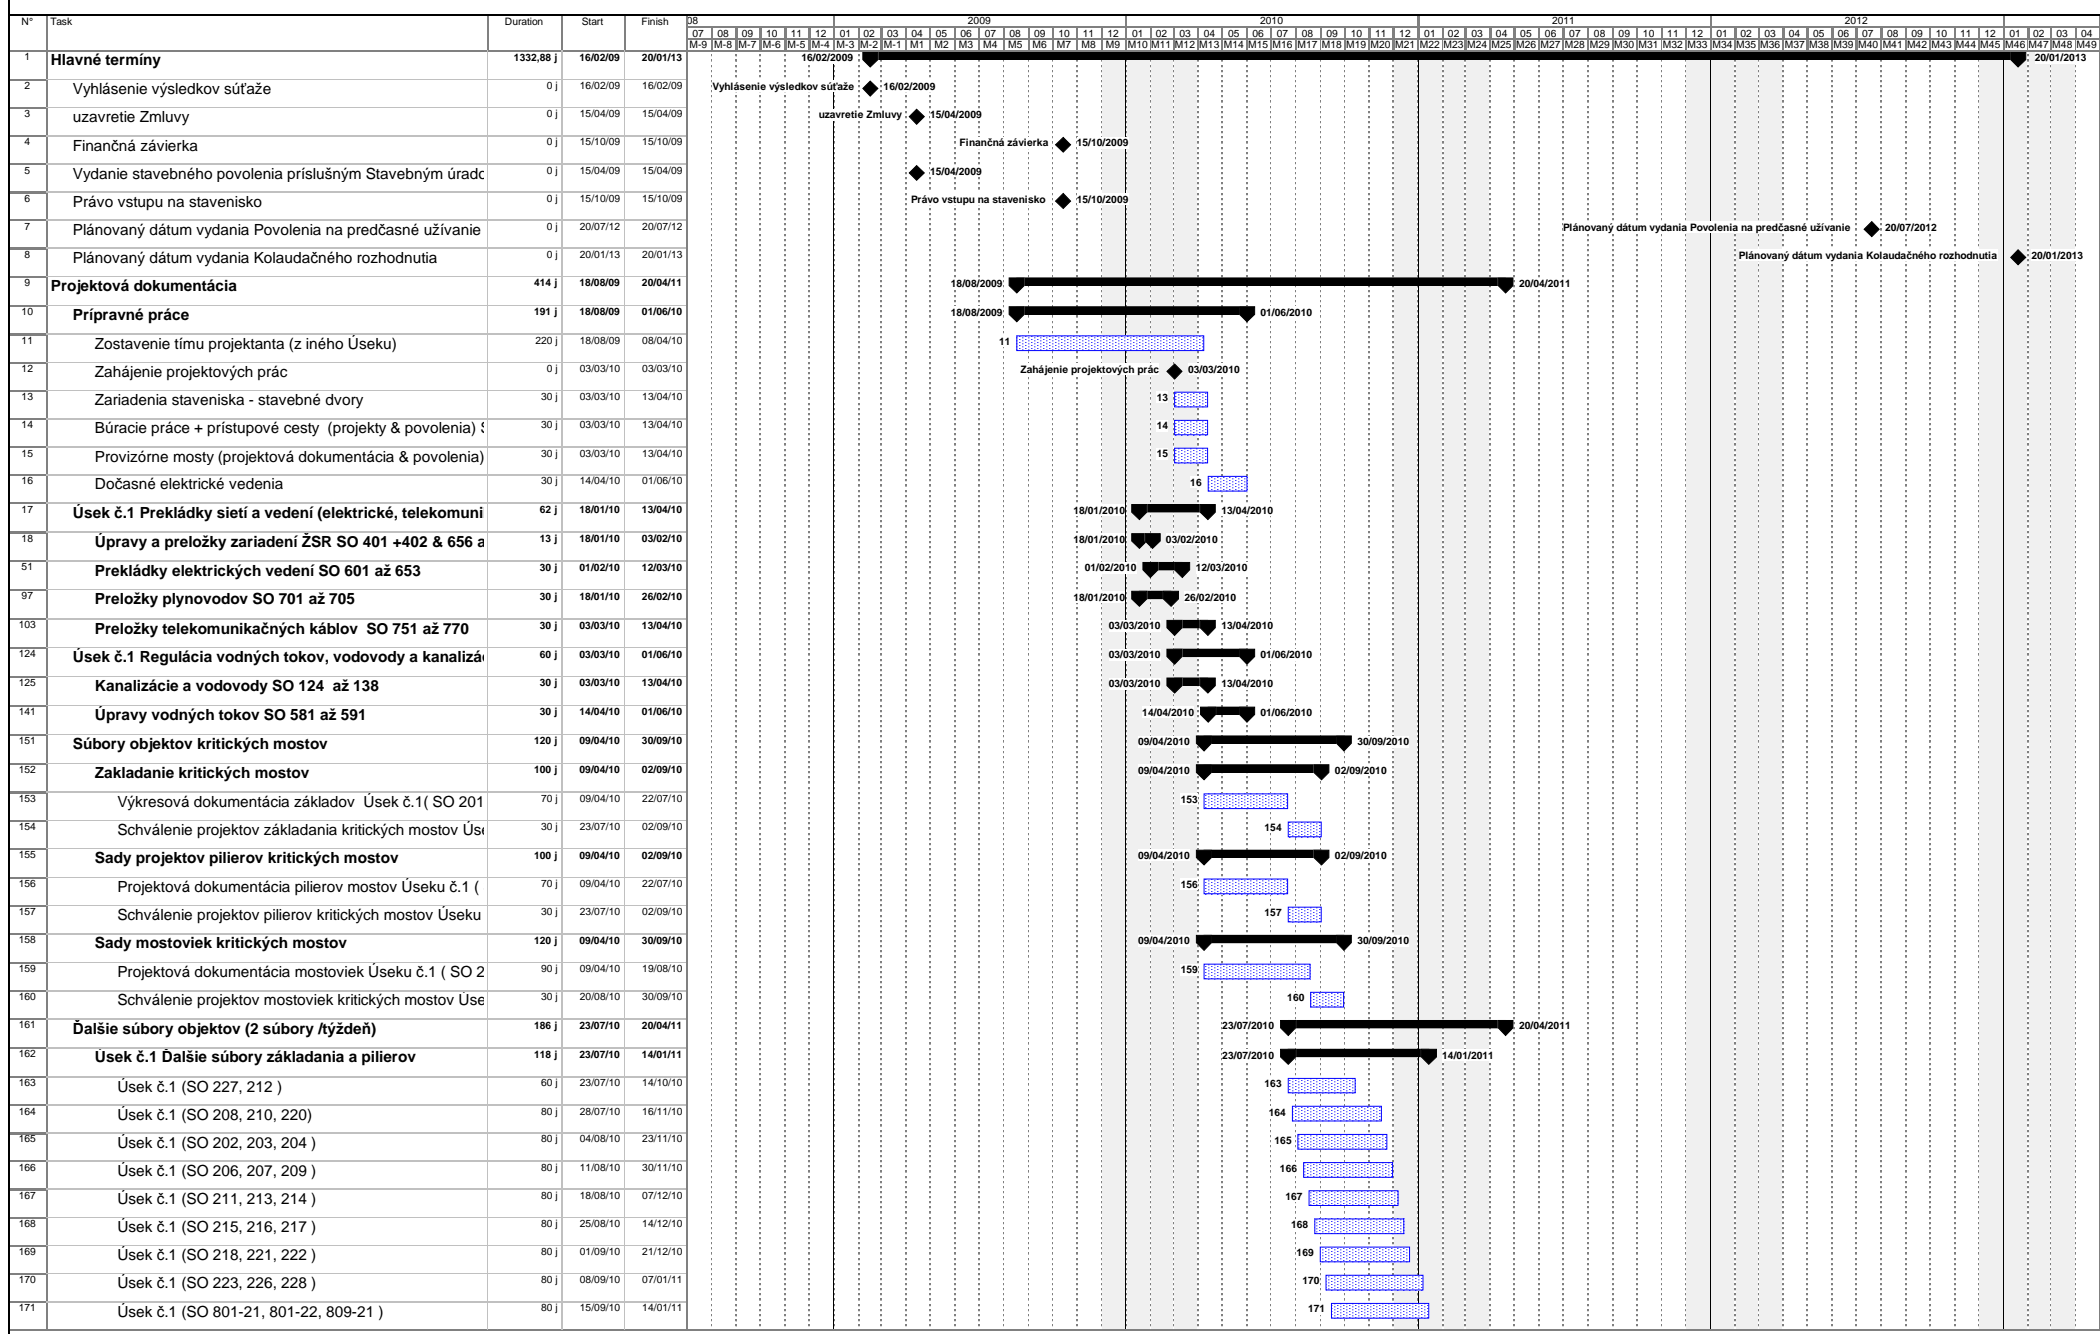

## SECTION 1 - DUBNÁ SKALA - TURANY

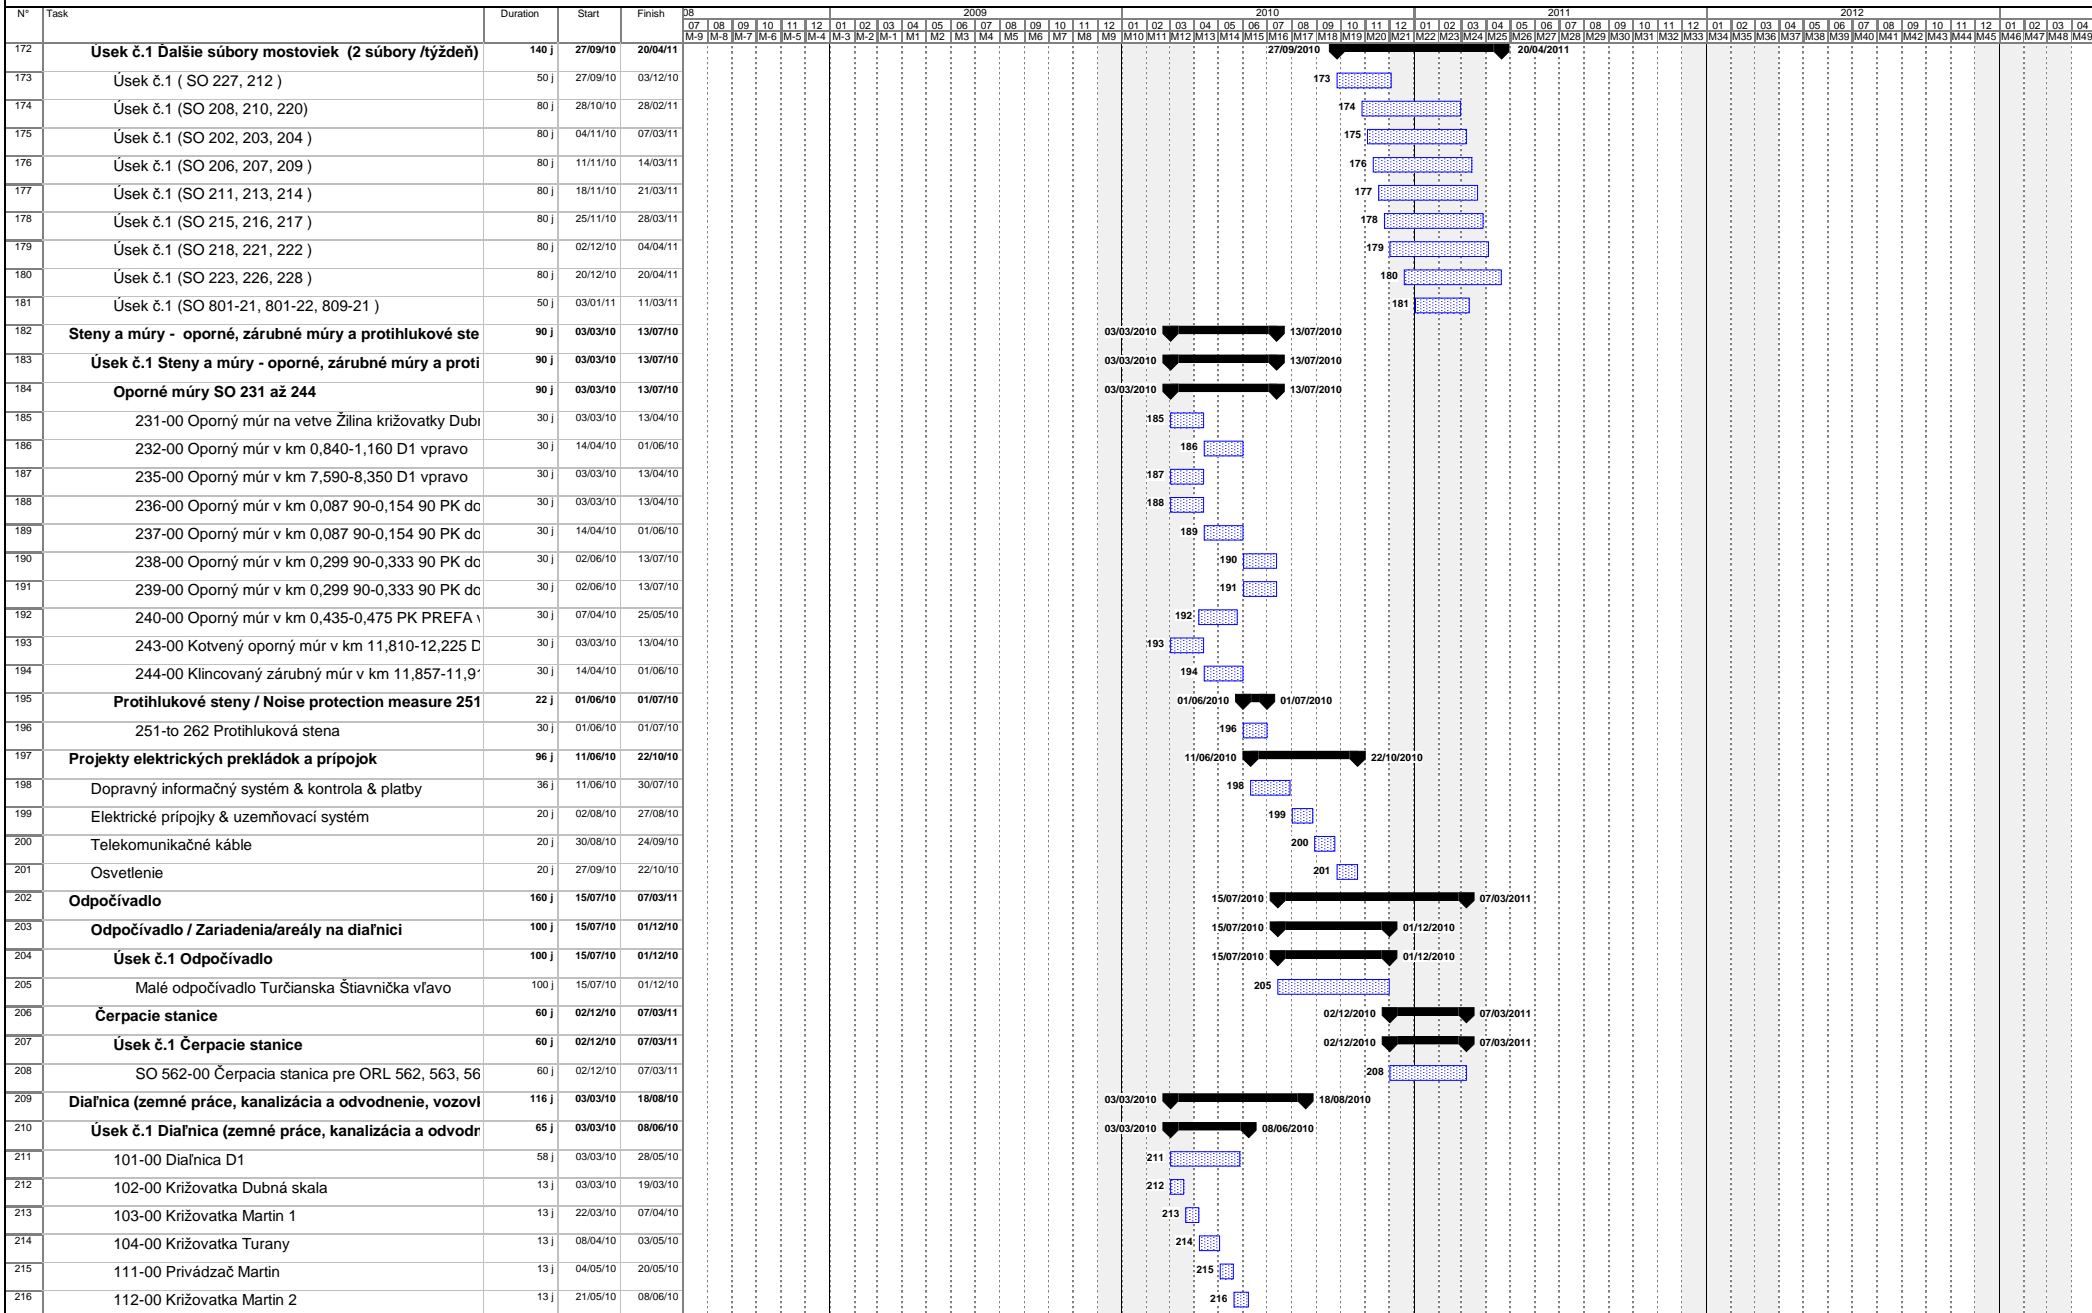








SECTION 1 - DUBNÁ SKALA - TURANY

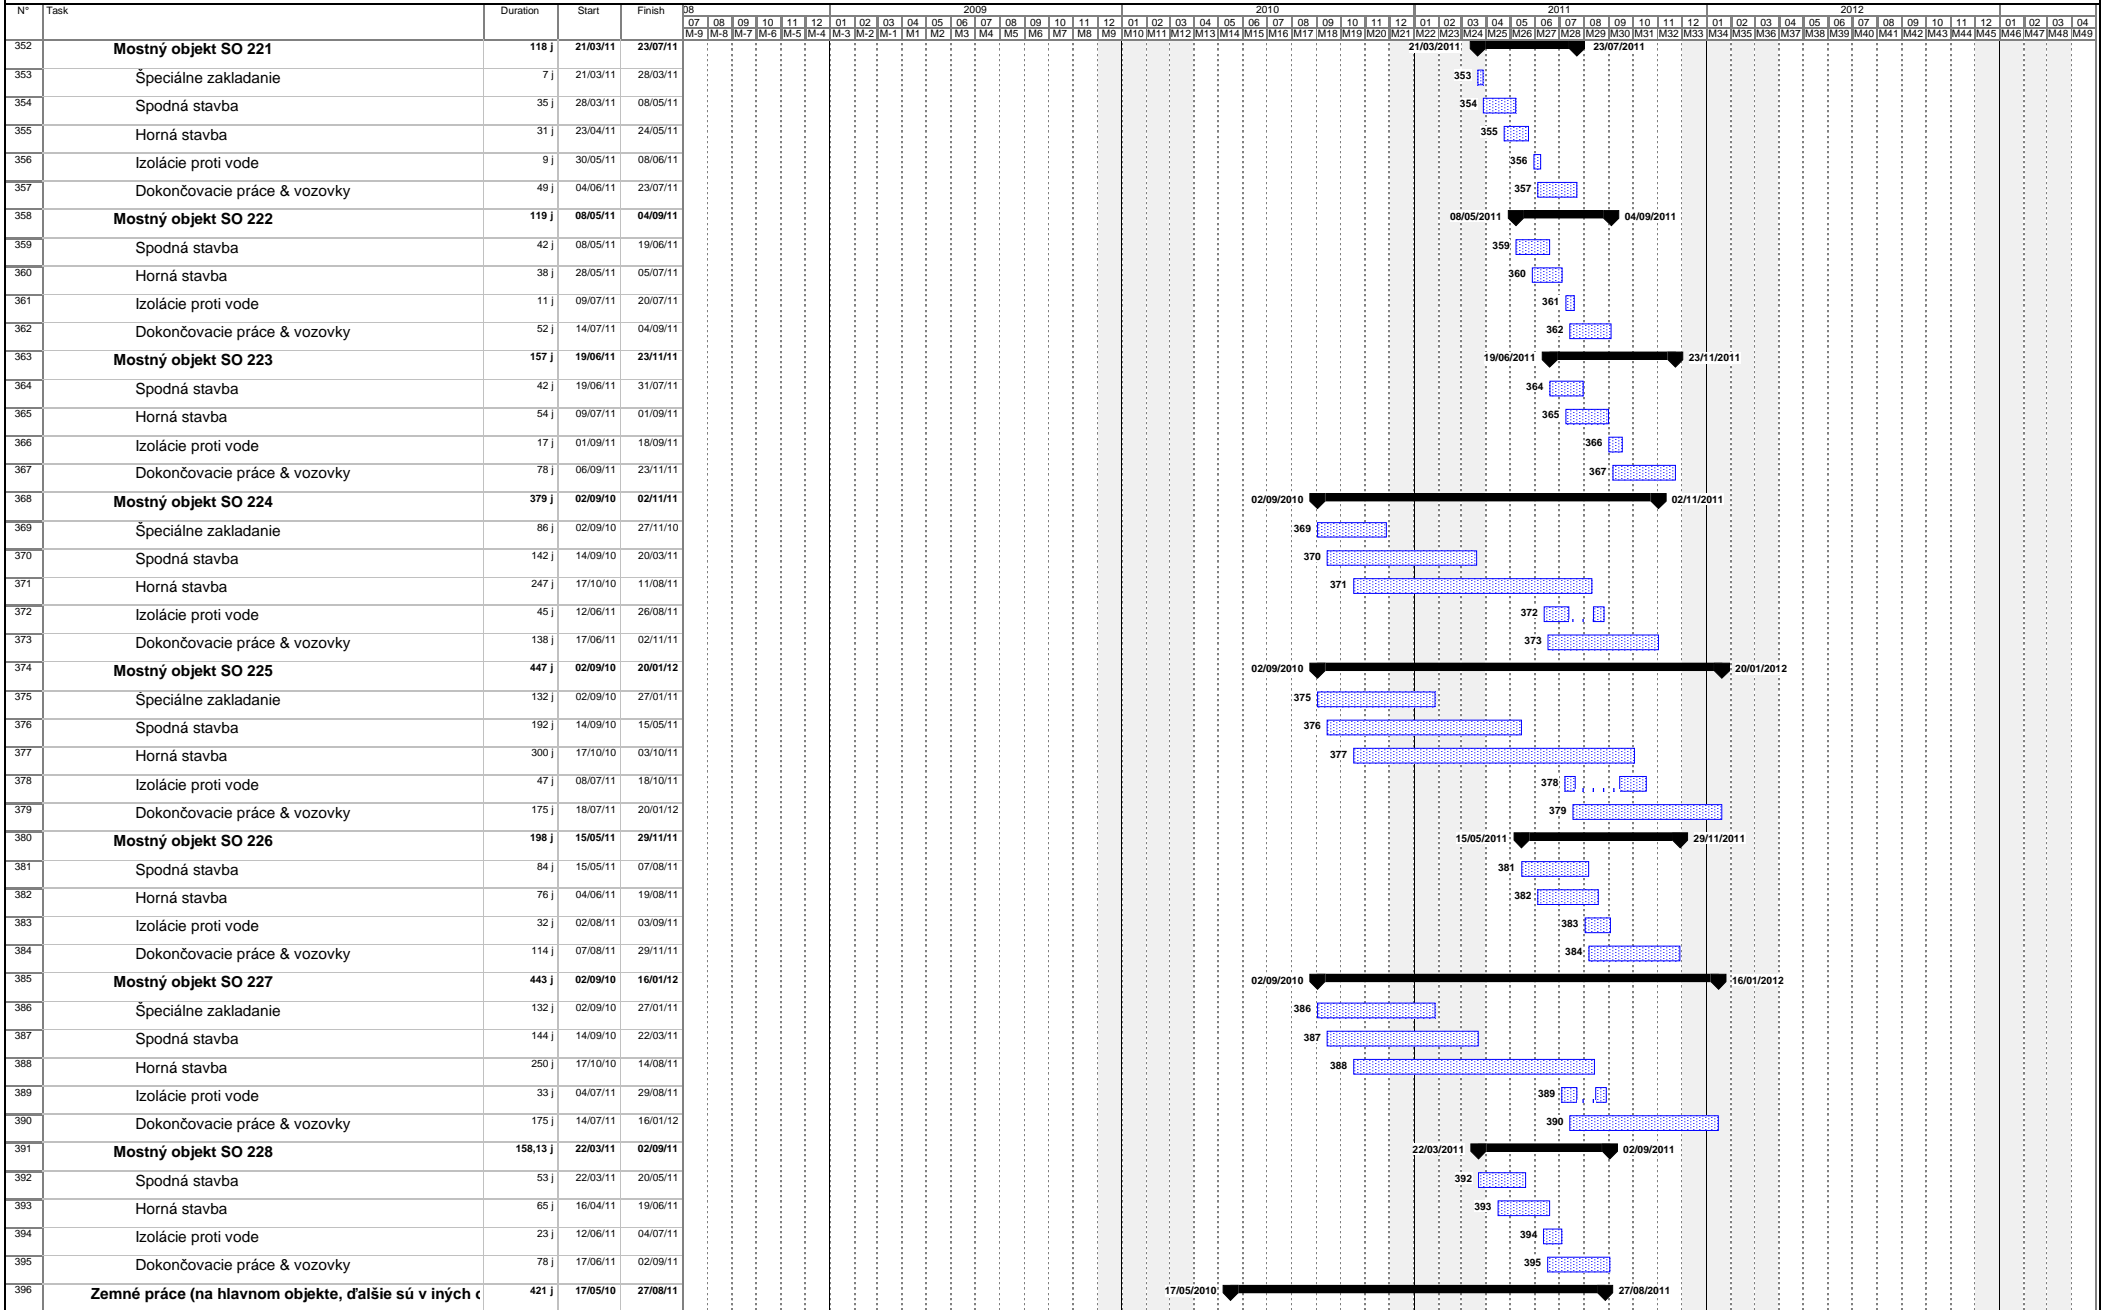



SECTION 1 - DUBNÁ SKALA - TURANY

N°	Task	Duration	Start	Finish	2009												2010												2011												2012												
					07	08	09	10	11	12	01	02	03	04	05	06	07	08	09	10	11	12	01	02	03	04	05	06	07	08	09	10	11	12	01	02	03	04	05	06	07	08	09	10	11	12	01	02	03	04	05	06	07
397	<b>Diaľnica SO 101, 111</b>	295,13 j	29/05/10	25/07/11																																																	
398	Zemné práce 01: 0,850 až 7,700 km	120 j	29/05/10	26/09/10																																																	
399	Zemné práce 02: 8,00 až 16,400 km	200 j	29/05/10	15/04/11																																																	
400	Zemné práce 03: zemné práce 2.etapa	130 j	11/11/10	25/07/11																																																	
401	Cesty SO 121 až 171	210 j	24/09/10	26/08/11																																																	
402	Mimoúrovňové križovatky SO 102, 103, 104 a SO 112	230 j	05/09/10	27/08/11																																																	
403	<b>Oporné múry</b>	299 j	17/05/10	25/04/11																																																	
404	Oporný múr SO 231	48 j	17/05/10	03/07/10																																																	
405	Oporný múr SO 232	184 j	16/07/10	31/01/11																																																	
406	Oporný múr SO 235	200 j	01/06/10	17/12/10																																																	
407	Oporný múr SO 236	116 j	01/06/10	24/09/10																																																	
408	Oporný múr SO 237	116 j	16/07/10	09/11/10																																																	
409	Oporný múr SO 238	52 j	09/11/10	31/12/10																																																	
410	Oporný múr SO 239	107 j	09/11/10	16/04/11																																																	
411	Oporný múr SO 240	64 j	31/12/10	25/04/11																																																	
412	Oporný múr SO 243	180 j	13/06/10	10/12/10																																																	
413	Oporný múr SO 244	86 j	16/07/10	10/10/10																																																	
414	Ukončenie výstavby oporných múrov	0 j	25/04/11	25/04/11																																																	
415	<b>Odvodnenie</b>	289 j	01/11/10	02/10/11																																																	
416	Ryhy pre uloženie drenáže SO 501 až 509	250 j	01/11/10	24/08/11																																																	
417	Bočné odvodnenie SO 501 až 509	250 j	16/11/10	08/09/11																																																	
418	Potrubia SO 501 až 509 & SO 562 až 568	250 j	16/11/10	08/09/11																																																	
419	Výpustný objekt SO 562 až 568	224 j	01/11/10	29/07/11																																																	
420	Regulácia prípojky SO 562 až 568 + SO 562-11 až 568	100 j	25/06/11	02/10/11																																																	
421	<b>Ďalšie práce</b>	625,13 j	03/02/10	13/12/11																																																	
422	Prekládka VN el. vedenia SO 601 až 633	180 j	01/04/10	04/10/10																																																	
423	Prekládka NN el. vedenia SO 636 až 653	79 j	01/04/10	25/06/10																																																	
424	Prekládka telekomunikačných káblov SO 751 až 759	143 j	13/04/10	09/09/10																																																	
425	Prekládka optických káblov SO 760 až 770	195 j	13/04/10	31/10/10																																																	
426	Prekládka potokov & úprava vodných diel SO 581 až 589	298 j	13/04/10	24/03/11																																																	
427	Prekládka vodovodov SO 520 až 540	163 j	13/04/10	29/09/10																																																	
428	Prekládka plynovodov SO 701 až 705	150 j	01/04/10	04/09/10																																																	
429	Úprava fasád a priečelií budov SO 217 až 274	28 j	09/07/10	06/08/10																																																	
430	Obnova jestvujúcich železničných tratí SO 331, 401, 402 a 403	76 j	03/02/10	26/04/10																																																	
431	Prekládka dočasného trakčného vedenia SO 656 až 660	218 j	03/02/10	15/09/10																																																	
432	Kanalizácia	304 j	13/04/10	30/03/11																																																	
433	Oplotenie SO 301 až SO 304	200 j	28/05/11	13/12/11																																																	
434	<b>Vozovky</b>	265 j	04/04/11	21/05/12																																																	
435	Diaľnica SO 101 až 111	200 j	14/06/11	21/05/12																																																	
436	Mimoúrovňové križovatky SO 102, 103, 104 a 112	53 j	04/04/11	01/06/11																																																	
437	<b>Iné cesty</b>	338 j	09/07/10	29/07/11																																																	
438	Prekládky ciest / obchádzky SO 041 až 048 + SO 51 až 57	338 j	09/07/10	29/07/11																																																	
439	Prekládka obslužných ciest Relocation of cart road SC	338 j	09/07/10	29/07/11																																																	
440	Úprava hlavných ciest SO 041 až 048 + SO 51 až 57	338 j	09/07/10	29/07/11																																																	
441	Búracie práce SO 001 až 036	153 j	09/07/10	09/12/10																																																	



## SECTION 1 - DUBNÁ SKALA - TURANY

